



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**

15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 1

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

COPY
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

ORDER DATE: 08/02/21		BUYER: BCARTERLANSAW		REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS		F.O.B.: FOB DESTINATION		DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION		UNIT PRICE		EXTENSION
<p>This Purchase is in accordance with Hernando County Contract No.21-C00008/DK - Construction of Hernando County Fire Station #5, BOCC Approved on: 7/13/2021, Doc ID No. 18536-A.</p> <p>The Construction of Fire Station #5 is located at 9490 Eldridge Rd., Spring Hill, Florida 34608</p> <p>The Contract Terms and Conditions apply, and the Purchase Order Terms and Conditions do not apply to this purchase.</p> <p>The County Contact Person is: . Erik Van De Boogaard, Hernando County Construction Projects Coordinator , Phone Number: (352) 754-4096 Ext 17037</p> <p>The Contractor Contact is: Lazaro Fernandez, Vice President Phone Number: (813) 200-8340</p> <p>9/28/2021 Change Order 1 TM New Vista has obtained various proposals for the requested scope to provide signalization per "T" drawings, with required stripping and maintenance of traffic. It is our opinion that Traffic Controls</p>							

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF COPY

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 2

V
E
N
D
O
R
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

Copy
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

ORDER DATE:08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS				F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -		
ITEM#	QUANTITY	UOM	DESCRIPTION					UNIT PRICE	EXTENSION
Products has the best all inclusive proposal to accomplish the scope required , and we find the price to be fair and reasonable. Price is only good for 10/8/21. Construction Contract #21-C00008/DK.									
ADD LINE 7 - Signalization FOR QUANTITY \$243,537.38 PER UNIT PRICE OF \$1.00									
NEW PO BALANCE WILL BE \$5,316,055.38									
2261-5606359 7 146122.43									
2491-5606359 7 97414.95									
06/01/2022 Change Order 2 JG NEW VISTA BUILDERS CONSTRUCTION 21-C0008/DK FIRE ST #5 REQUEST FOR EXTENSION OF DAYS TO COMPLETE THE JOB. NO COST TO THIS CHANGE ORDER.									
it is requested that the project be extended by 167 days to substantial completion. The new date for substantial completion shall be November 22, 2022. Final completion December 22, 2022.									
06/02/2022 Change Order 3 JG									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 3

V
E
N
D
O
R
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP, LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF Copy

S
H
P
T
O
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
CONTRACT # 21-C00008/DK CONSTRUCTION OF HERNANDO COUNTY FIRE STATION #5 ADD A LINE FOR CHANGE ORDER #3 FOR ADDITIONAL WORK, LABOR AND MATERIALS. FOR UNDERGROUND PER WREC POWER RELOCATION, DOOR HARDWARE CHNAGES DUE TO 5/4/22 REVISED PLANS AND PROVIDE, PICKUP 25 SIMPSON PBS66 FENCE POST BASE. ADD LINE 8 - LUMP SUM FOR ADDITIONAL WORK QTY. \$41,333.51, UNIT PRICE 1.00 NEW PO BALANCE WILL BE \$5,357,388.89 2261-5606359 8 24800.11 2491-5606359 8 16533.40 8/22/22 - Change Order 4 - DK - Material Increases request, Due to Market fluctuation from time of Bid. Add additional funds. This change order is based solely on direct cost elements such as labor, material, and normal markups, and does not include any amount for changes in the sequence of work, delays, disruption, rescheduling, extended overhead, acceleration, and/or impact costs which arenot possible to assess at the present time.									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 4

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF Copy

HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601
TO

ORDER DATE:08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
Line 8 - Increase \$200,341.81 (RCO#1) New Line Balance will be \$241,675.32									
9/1/22 - Change Order 5 - DK - CHANGE ORDER REQUESTS RCO#7, 10,14,15,16,17,18,19,20,21. ADDITION OF \$121,903.65 TO LINE 8 ADDITIONAL 5 DAYS REQUESTED ON 2 DAYS ON RCO# 7 & 3 DAYS ON RCO# 16. NEW COMPLETION DATE WILL BE 12/27/2022									
9/19/22 - Change Order 6 - DK - CHANGE ORDER REQUEST FOR MATERIAL INCREASE COSTS AND ITEMS NO LONGER AVAILABLE SINCE PROJECT BEGAN. ADDITIONAL FUNDS AND EXTRA DAYS REQUEST.									
RCO#23 - CONCRETE MATERIAL INCREASE - \$9,491.01 RCO#24 - SIGN CHANGES - INCREASE \$5,607.95 ADD 10 DAYS RCO#25 - FAN NO LONGER AVAILABLE - \$883.15 RCO#26 - CHANGE IN WASHER AND DRYER- \$17,046.27 RCO#27 - ROLL UP DOORS - \$13,022.44 ADD 20 DAYS RCO#28 - ASPHALT SURCHARGE - \$4,097.36									
TOTAL FUNDS ADDITION TO THIS PO FOR THESE CHANGES WILL									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 5

**V
E
N
D
O
R** [bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

Copy
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
<p>BE \$50,148.18.</p> <p>30 EXTRA DAYS ADDED WILL MAKE THE COMPLETION DATE JAN. 26, 2023.</p> <p>NEW LINE BALANCE WILL BE \$413,727.15</p> <p>NEW PO BALANCE WILL BE \$5,729,782.53</p> <p>12/21/2022 Change Order 7 JG</p> <p>A BUDGET AMENDMENT WAS APPROVED ON 11/29/22. IT IS ATTACHED.</p> <p>ADD ADDITIONAL 10 DAYS. NEW FINAL COMPLETION DATE WILL BE JAN. 1, 2023.</p> <p>CONTRACT # 21-C00008/DK CONSTRUCTION OF HERNANDO COUNTY FIRE STATION #5.</p> <p>INCREASE FUNDS FOR RCO# 29 through 37.</p> <p>29 Door lite changes \$1,466.36</p> <p>30 Casework increases \$23,690.25</p> <p>31 HRU circuit wiring \$2,179.56</p> <p>32 Fiber optic routing \$21,213.02</p>									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF

[Signature]

****SEE TERMS AND CONDITIONS ON REVERSE SIDE****

APPROVED BY:

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 6

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP, LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF Copy

HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601
TO

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
	33		Change sign (\$567.52)						
	34		Work table changes				\$15,917.56		
	35		Cost increase halo lit				\$1,663.08		
	36		Change exterior letters				\$572.99		
	37		Murphy beds framing/blocking				\$22,126.86		
			TOTAL				\$88,262.16		
LINE 8 - INCREASE \$88,262.16									
NEW LINE BALANCE WILL BE \$501,989.31									
NEW PO BALANCE WILL BE \$5,778,331.72									
2261-5606359 8 52957.30									
12/30/2022 Change Order 8 JG									
CONTRACT 21-C00008/DK CONSTRUCTION OF FIRE STATION NO. 5.									
Time Extension Request for 104 extra days. Final Completion date is currently Jan. 1, 2023. It has been impacted with CO's received to date and other delays related to drywall, concrete delivery/availability, and delay in obtaining soffit materials.									
New final completion date will be April 14, 2023									
01/18/2023 Change Order 9 JG									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

[Signature]

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 7

V
E
N
D
O
R
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

Copy
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]
T
O

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
CONTRACT 21-C00008/DK CONSTRUCTION OF FIRE STATION NO. 5. RCO# 38-42, Plus Time Extension Request for 10 extra days. Final Completion date is currently Friday April 14, 2023. RCO# 38 - alert paging system installation = \$18,060.94 RCO# 39 - Circuit Wiring for Oil Separator = \$2,251.52 RCO# 40 - Change to SS1 Sink (New Sink) = \$3,642.71 RCO# 41 - Credit to use 7.5HP compressor = (-\$1,995.00) RCO# 42 - Extractor circuit = \$1,307.00 Line 8 - Increase \$23,267.17 New Line Balance will be \$525,256.48 Total cost to add to contract is \$23,267.17 New PO Balance will be \$5,841,311.86 New substantial completion date will be March 24, 2023. New final completion date will be Monday April 24, 2023									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 8

V
E
N
D
O
R

bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP, LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610

PDF

Copy
S
H
P
T
O

HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
2261-5606359 8 13960.30									
04/10/2023 Change Order 10 JG CONTRACT # 21-C00008/DK OF FIRE STATION #5 construction is located at 9252 Spring Hill Drive, Spring Hill, Florida. RCO@s 43-44-45-47-48-49-50-51-52-53-54-55-56, (Total Credit of -\$6,576.47). Substantial Completion Date is April 30, 2023. Final Completion Date is May 30, 2023.									
RCO#43 - Per RFI#60, Connect Condensate Lines to Roof Drain Pipes - \$1,549.55 RCO#44 - Manitowoc Appliance Price Increases as of 1/1/23 - \$1,462.87 RCO#45 - Residential Appliance Cost Increases, as of 1/23/23. Submittal was Submitted on 10/18/22 and Approved on 1/6/23 - \$2,493.19 RCO#47 - Per RFI#69 response, Add 1 Type N Fixture on East Side of Building - \$804.90 RCO#48 - Per RFI#71, Install 1 SA 2 Pole Breaker for Kitchen Exhaust Fan - \$489.36 RCO#49 - Per RFI#70, Provide Feed from P1 to Control Panel Location - \$2,914.00									
ITEM#	ACCOUNT			AMOUNT		PROJECT CODE		PAGE TOTAL \$	
								TOTAL \$	

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 9

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF Copy

HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601
TO

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
RCO#50 - Replace Sandusky Storage Cabinet with Uline Product - \$2,230.64									
RCO#51 - Change Murphy Beds Color from Chocolate to Linear Ash. LT on this product is 4-6 weeks from the date order is placed (pending owner's approval). Once we have a confirmation on delivery we will be able to determine if it has any impact to project schedule - \$1,710.10									
RCO#52 - Change Corner Guards to Stainless Steel CO-8 Surface Mounted - (\$787.70)									
RCO#53 - Irrigation & Landscaping Cost Increases - \$2,3									
5/22/23 Change order 11 - FH									
CONTRACT # 21-C00008/DK OF FIRE STATION #5									
construction is located at 9252 Spring Hill Drive, Spring Hill, Florida.									
No Cost Change for this change order.									
Time Extension Request from New Vista.									
Extend 62 days from current final completion date of 5/30/2023 to 7/31/23									
Substantial Completion Date extended 61 days from 4/30/23 to 6/30/2023.									

ITEM#	ACCOUNT	AMOUNT	PROJECT CODE	PAGE TOTAL \$
				TOTAL \$

PDF Copy

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 10

**V
E
N
D
O
R** [bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

COPY
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

PDF

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW			REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION			DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION				UNIT PRICE		EXTENSION
Final Completion Date is July 31, 2023.									
03	999999.00	JOB	HERNANDO COUNTY FIRE STATION #5 - CONSTRUCTION PROJECT - CONTRACT # 21-C00008/DK				1.0000		999,999.00
04	999999.00	JOB	HERNANDO COUNTY FIRE STATION #5 - CONSTRUCTION PROJECT - CONTRACT # 21-C00008/DK				1.0000		999,999.00
05	999999.00	JIOB	HERNANDO COUNTY FIRE STATION #5 - CONSTRUCTION PROJECT - CONTRACT # 21-C00008/DK				1.0000		999,999.00
06	69747.67	JOB	HERNANDO COUNTY FIRE STATION #5 - CONSTRUCTION PROJECT - CONTRACT # 21-C00008/DK				1.0000		69,747.67
07	239736.24	EA	SIGNALIZATION				1.0000		239,736.24
08	525256.48	EA	LUMP SUM FOR ADDITIONAL WORK				1.0000		525,256.48

ITEM#	ACCOUNT		AMOUNT	PROJECT CODE	PAGE TOTAL \$ 3,834,737.39	
					TOTAL	\$ 3,834,737.39
03	02261	5606359	599,999.40	PRINT COPY		
03	02491	5606359	399,999.60			
04	02261	5606359	599,999.40			
04	02491	5606359	399,999.60			
05	02261	5606359	599,999.40			
05	02491	5606359	399,999.60			
06	02261	5606359	43,841.60			
06	02491	5606359	27,899.07			
07	02261	5606359	143,841.75			
07	02491	5606359	95,894.49			

****SEE TERMS AND CONDITIONS ON REVERSE SIDE****

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11

PAGE NO. 11

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP, LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

COPY
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]
TO

ORDER DATE: 08/02/21			BUYER: BCARTERLANSAW				REQ. NO.: RQ211146		REQ. DATE: 09/30/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION				DESC.: CONTRACT # 21-C00008/DK -			
ITEM#	QUANTITY	UOM	DESCRIPTION					UNIT PRICE		EXTENSION

ITEM#	ACCOUNT		AMOUNT	PROJECT CODE	PAGE TOTAL \$	
					TOTAL \$	
08	02261	5606359	315,153.90			
08	02491	5606359	210,102.58			

PDF COPY

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident



**HERNANDO COUNTY
BOARD OF COUNTY COMMISSIONERS**
15470 FLIGHT PATH DR
BROOKSVILLE, FL 34604

PURCHASE ORDER-CHANGE NO. 21001040-11
CHANGE DATE: 05/22/23

PAGE NO. 1

VENDOR
[bids@newvistabuildersgroup.com
86525
NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA FL 33610]

PDF

COPY
[HC CONSOLIDATED FIRE
HC FIRE LOGISTICS
60 VETERANS AVE
BROOKSVILLE, FL 34601]

ORDER DATE: 08/02/21		BUYER: BCARTERLANSAW		REQ. NO.: RQ211146		REQ. DATE: 07/26/21	
TERMS: NET 30 DAYS			F.O.B.: FOB DESTINATION		DESC.: CHANGE ORDER - 11		
ITEM#	QUANTITY	UOM	DESCRIPTION			UNIT PRICE	EXTENSION
<p>5/22/23 Change order 11 - FH CONTRACT # 21-C00008/DK OF FIRE STATION #5 construction is located at 9252 Spring Hill Drive, Spring Hill, Florida.</p> <p>No Cost Change for this change order.</p> <p>Time Extension Request from New Vista. Extend 62 days from current final completion date of 5/30/2023 to 7/31/23</p> <p>Substantial Completion Date extended 61 days from 4/30/23 to 6/30/2023.</p> <p>Final Completion Date is July 31, 2023.</p>							
04	.00		JOB HERNANDO COUNTY FIRE STATION #5 - CONSTRUCTION PROJECT - CONTRACT # 21-C00008/DK			.0000	.00

ITEM#	ACCOUNT		AMOUNT	PROJECT CODE	PAGE TOTAL \$.00
04	02261	5606359	.00		TOTAL \$.00
04	02491	5606359	.00			

PDF COPY

SEE TERMS AND CONDITIONS ON REVERSE SIDE

APPROVED BY:

[Signature]

CHIEF PROCUREMENT OFFICER

HERNANDO COUNTY PURCHASE ORDER TERMS AND CONDITIONS

GENERAL

The condition of this order may not be changed by Vendor/Contractor. If order is not acceptable, return to Hernando County Purchasing and Contracts Department. Failure of a Vendor/Contractor to deliver according to this purchase order awarded to him or to comply with any of the terms and conditions therein may disqualify him from receiving future orders.

QUALITY

All material or services furnished on this order must be as specified and subject to County inspection and approval within a reasonable time after delivery at destination. Variations in materials or services from those specified in this order must not be made without written authority from the Chief Procurement Officer. Materials rejected will be returned at the Vendor/Contractor's risk and expense.

QUANTITY/PRICE

The quantity of materials ordered or the prices specified must not be exceeded without written authority being first obtained from the Chief Procurement Officer.

INDEMNITY AND INSURANCE

The Vendor/Contractor agrees to indemnify and hold harmless Hernando County, including its officers, agents and employees, from all claims, damages, losses and expenses, including reasonable attorneys' fees, and costs brought or incurred on account of injuries or damages sustained by any party due to the operations of the Vendor/Contractor under this contract. The Vendor/Contractor further agrees to provide workers' compensation for all employees, and to maintain such general and auto liability insurance as is deemed necessary by the County for the particular circumstances and operations of the Vendor/Contractor. The Vendor/Contractor further agrees to provide the County with Certificates of Insurance, indicating the amount of coverage in force, upon request.

PACKING

Packages must be plainly marked with shipper's name and purchase order number; charges are not allowed for boxing or crating unless previously agreed upon in writing.

DELIVERY

All materials must be shipped F. O. B. destination. The County will pay no freight or express charges, except by previous agreement. If specific purchase is negotiated on the basis of F.O.B. shipping point, VENDOR/CONTRACTOR ARE TO PREPAY SHIPPING CHARGES AND ADD TO INVOICE. Delivery must actually be affected within the time stated on purchase made between 8:00 AM and 5:00 PM Monday to Friday inclusive unless otherwise stated. In case of default by the Vendor/Contractor, Hernando County may procure the articles or services covered by this order from other sources and hold the Vendor/Contractor responsible for any excess occasioned thereby.

PAYMENT

Partial billing will be accepted only for items received within the specified delivery period. Payments for items delivered after this specified delivery period will be made after the entire order is completed and accepted by Hernando County. Payment shall be made in accordance with Florida Statute 218, Florida Prompt Payment Act. Payment for accepted equipment/supplies/services will be accomplished by submission of an invoice, in duplicate; to the Ship To Address on the front of the purchase order unless otherwise indicated.

MATERIAL SAFETY DATA SHEET

The Vendor/Contractor agrees to furnish Hernando County with a current Material Safety Data Sheet (MSDS) on or before delivery of each and every hazardous chemical or substance purchased which is classified as toxic under Florida Statute 442. Appropriate labels and MSDSs shall be provided for all shipments. Send MSDSs and other pertinent data to: Hernando County Purchasing and Contracts Department, 20 North Main Street, Room 365, Brooksville, FL 34601-2828.

OSHA REQUIREMENT

The Vendor/Contractor or contractor hereby guarantees Hernando County that all materials, supplies and equipment as listed on the purchase order meet the requirements, specifications and standards as provided for under the Federal Occupations Safety and Health Administration Act of 1970, as from time to time amended and in force at the date thereof.

LEGALLY AUTHORIZED WORKFORCE

VENDOR/CONTRACTOR represents and warrants that VENDOR/CONTRACTOR is in compliance with all applicable federal, state and local laws, including, but not limited to, the laws related to the requirement of an employer to verify an employee's eligibility to work in the United States. VENDOR/CONTRACTOR is encouraged (but not required) to incorporate the IMAGE best practices into its business and, when practicable, incorporate verification requirements into its agreements with subcontractors. The IMAGE Best Practices can be found on the COUNTY'S website at www.hernandocounty.us/pur/.

INSURANCE

Unless otherwise specified, the Contractor shall, at its sole expense, maintain in effect at all times during the performance of the services insurance coverage with limits not less than those set forth below (unless limits have been lowered) and with insurers and under forms of policies satisfactory to COUNTY.

<u>Coverage</u>	<u>Minimum Amounts and Limits</u>
(a) Worker's Compensation Employer's Liability	Statutory requirements at location of work \$ 100,000 each accident \$ 100,000 by employee \$ 500,000 policy limit
(b) Commercial General Liability (Additional Insured & Wavier Of Subrogation)	\$ 2,000,000 General Aggregate \$ 2,000,000 Products-Comp. Ops Agg. \$ 1,000,000 Each Occurrence
(c) Automobile Liability Option of Split Limits: (1.) Bodily Injury	\$ 5,000 Medical Expense \$ 1,000,000 Combined Single Limit (owned, hired and non-owned) \$ 1,000,000 Per Person or \$1,000,000 Per Accident

HERNANDO COUNTY

PURCHASING REVIEW FORM

Procurement Contract:	Fran Hallet
Contract purpose: (briefly describe)	21-C00008/DK – Fire Station #5 Construction
	PO 21001040
Vendor Name:	New Vista Builders Group LLC
REQ#ITB/ RFP/Q#:	Change Order 11
Received Document	

Procurement Agent Review:	<i>Fran Hallet</i>	5/18/23	Fran Hallet
	Signature	Date	Printed Name
Comments:	Change Order # 11 is a no cost change order to extend substantial completion 61 days from 4/30/23 to 6/30/23 and Final completion 62 days from 5/30/23 to 7/31/23. Extension is due to economic constraints in acquiring material, labor shortage, permitting and fabrication of cabinetry. No Issues		

Grant Review:			
	Signature	Date	Printed Name
Comments:	N/A		

Chief of Procurement Review:			
	Signature	Date	Printed Name
Comments:			
<div style="border: 2px solid black; border-radius: 15px; padding: 10px; display: inline-block;"> APPROVED <i>By Carla Rossiter-Smith at 11:46 pm, May 21, 2023</i> </div>			

Recommendation:	



Hernando County Board of County Commissioners
15470 Flight Path Dr.
Brooksville, FL 34604

Rev: 0

Construction Change Order

Owner: Hernando County Board of County Commissioners

Owner's Representative:

Vendor: NEW VISTA BUILDERS GROUP LLC

Change Order No. 11
Contract No. 21001040

Change Order Date: 05/18/2023
Contract Date:

Project Description:

FIRE STATION #5 CONSTRUCTION

The Project is Changed as Follows

Justification: CONTRACT # 21-C00008/DK OF FIRE STATION #5 construction is located at 9252 Spring Hill Drive, Spring Hill, Florida.

No Cost Change for this change order.

Time Extension Request from New Vista.
Extend 61 days from current final completion date of May 30, 2023.

Substantial Completion Date is June 30, 2023. Extended from 4/30/23

Final Completion Date is July 31, 2023. Extending from 5/30/23 o 7/31/23 is 62 days

Total Addition/Deduction this Change Order: .00

The Original Contract Sum was 5,072,518.00
Net Change by previously authorized Change Orders: 762,217.39
The Contract Sum prior to this Change Order was 5,834,735.39
The Net Amount of this Change Order is: .00
The new Contract Sum including this Change Order will be 5,834,735.39

The Contract Time will be changed by this Change Order (Days): 61
The Date of Substantial Completion as of the date of this Change Order therefore is:

Vendor Name/Address:

NEW VISTA BUILDERS GROUP LLC
6375 HARNEY RD
SUITE 105
TAMPA, FL 33610

Owner or Owner's Representative:

Hernando County Commission
15470 Flight Path Dr.
Brooksville, FL 34601

APPROVED

By Carla Rossiter-Smith at 11:45 pm, May 21, 2023

Authorized Signature

Date:

5/10/23

Chief Procurement Office

Date:

Distribution:

Vendor - Original
Purchasing & Contracts
Finance
Requisitioning
Contract File

[Signature] 5.18.2023



May 17, 2023

Attn.: Erik Van De Boogaard
Hernando County Construction Projects Coordinator
1525 E. Jefferson Street
Brooksville, FL 34601
Via: evandeboogard@co.hernando.fl.us

Reference: *Hernando County Fire Station #5*

Subject: *Time Extension*

Dear Erik:

Attached you will find the latest schedule update. It has been impacted with change orders received to date, and other delays we've encountered due to the economic constraints in acquiring materials, labor shortage, delay in procurement of stainless-steel cabinetry, permit for monument sign, fabrication of cabinetry.

New Vista will strive to improve the finish date as much as possible, currently, we have no control of the monument permit, therefore, we may have to review the schedule once that permit is released.

Therefore, respectfully, we request a time extension per the attached supporting document through July 31, 2023.

Should you have any questions please feel free to contact our office at 813-200-8340.


Sincerely,


Lazaro Fernandez

Lazaro Fernandez
Vice President

Cc: Michael Langiano / NVBG
Cc: Chumany Richardson / NVBG

6375 Harney Rd, Suite 105
Tampa, FL 33610
Tel: 813-200-8340
Fax: 813-354-4846
Info@newvistabuildersgroup.com
CGC057992, CGC1508551

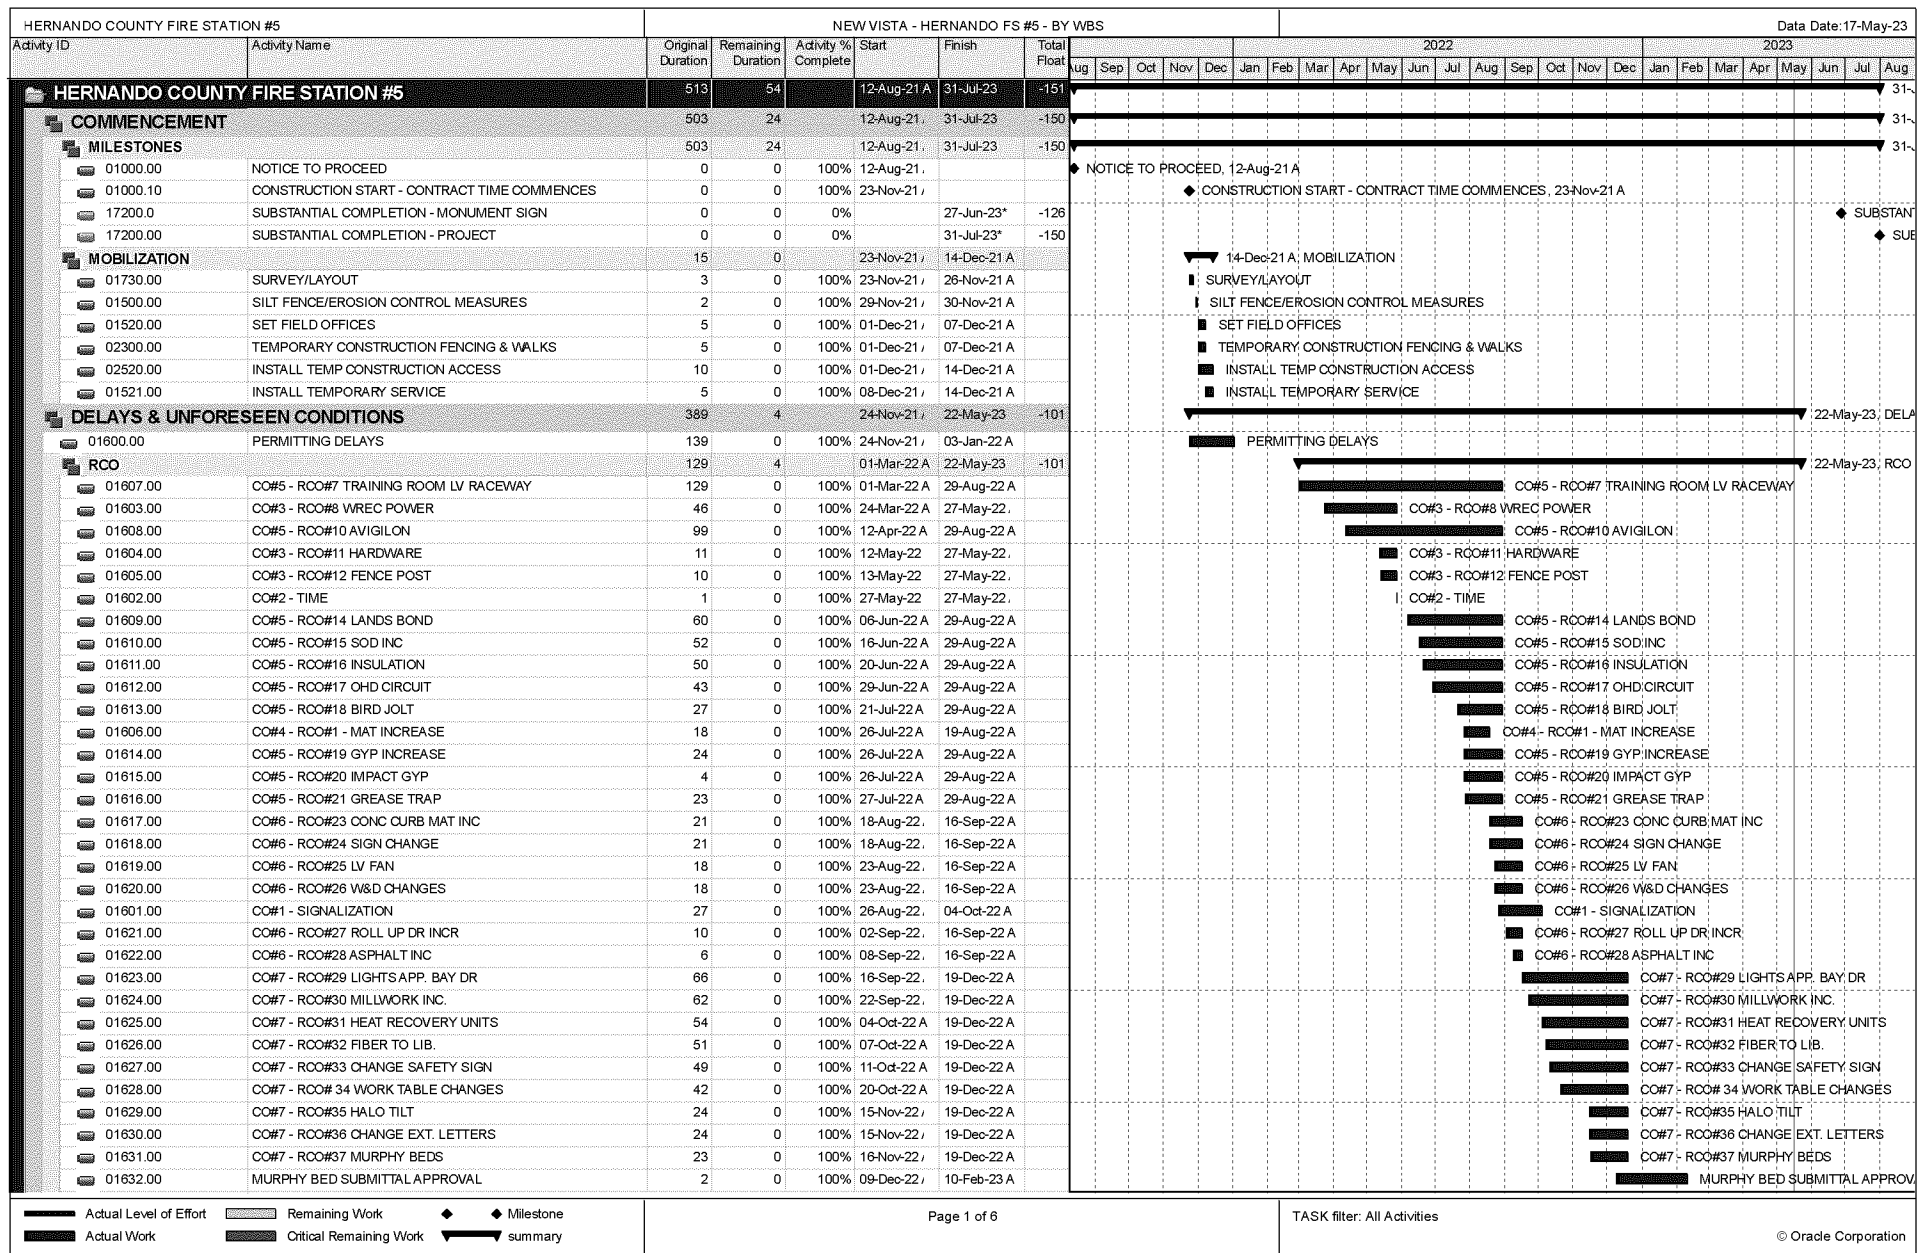


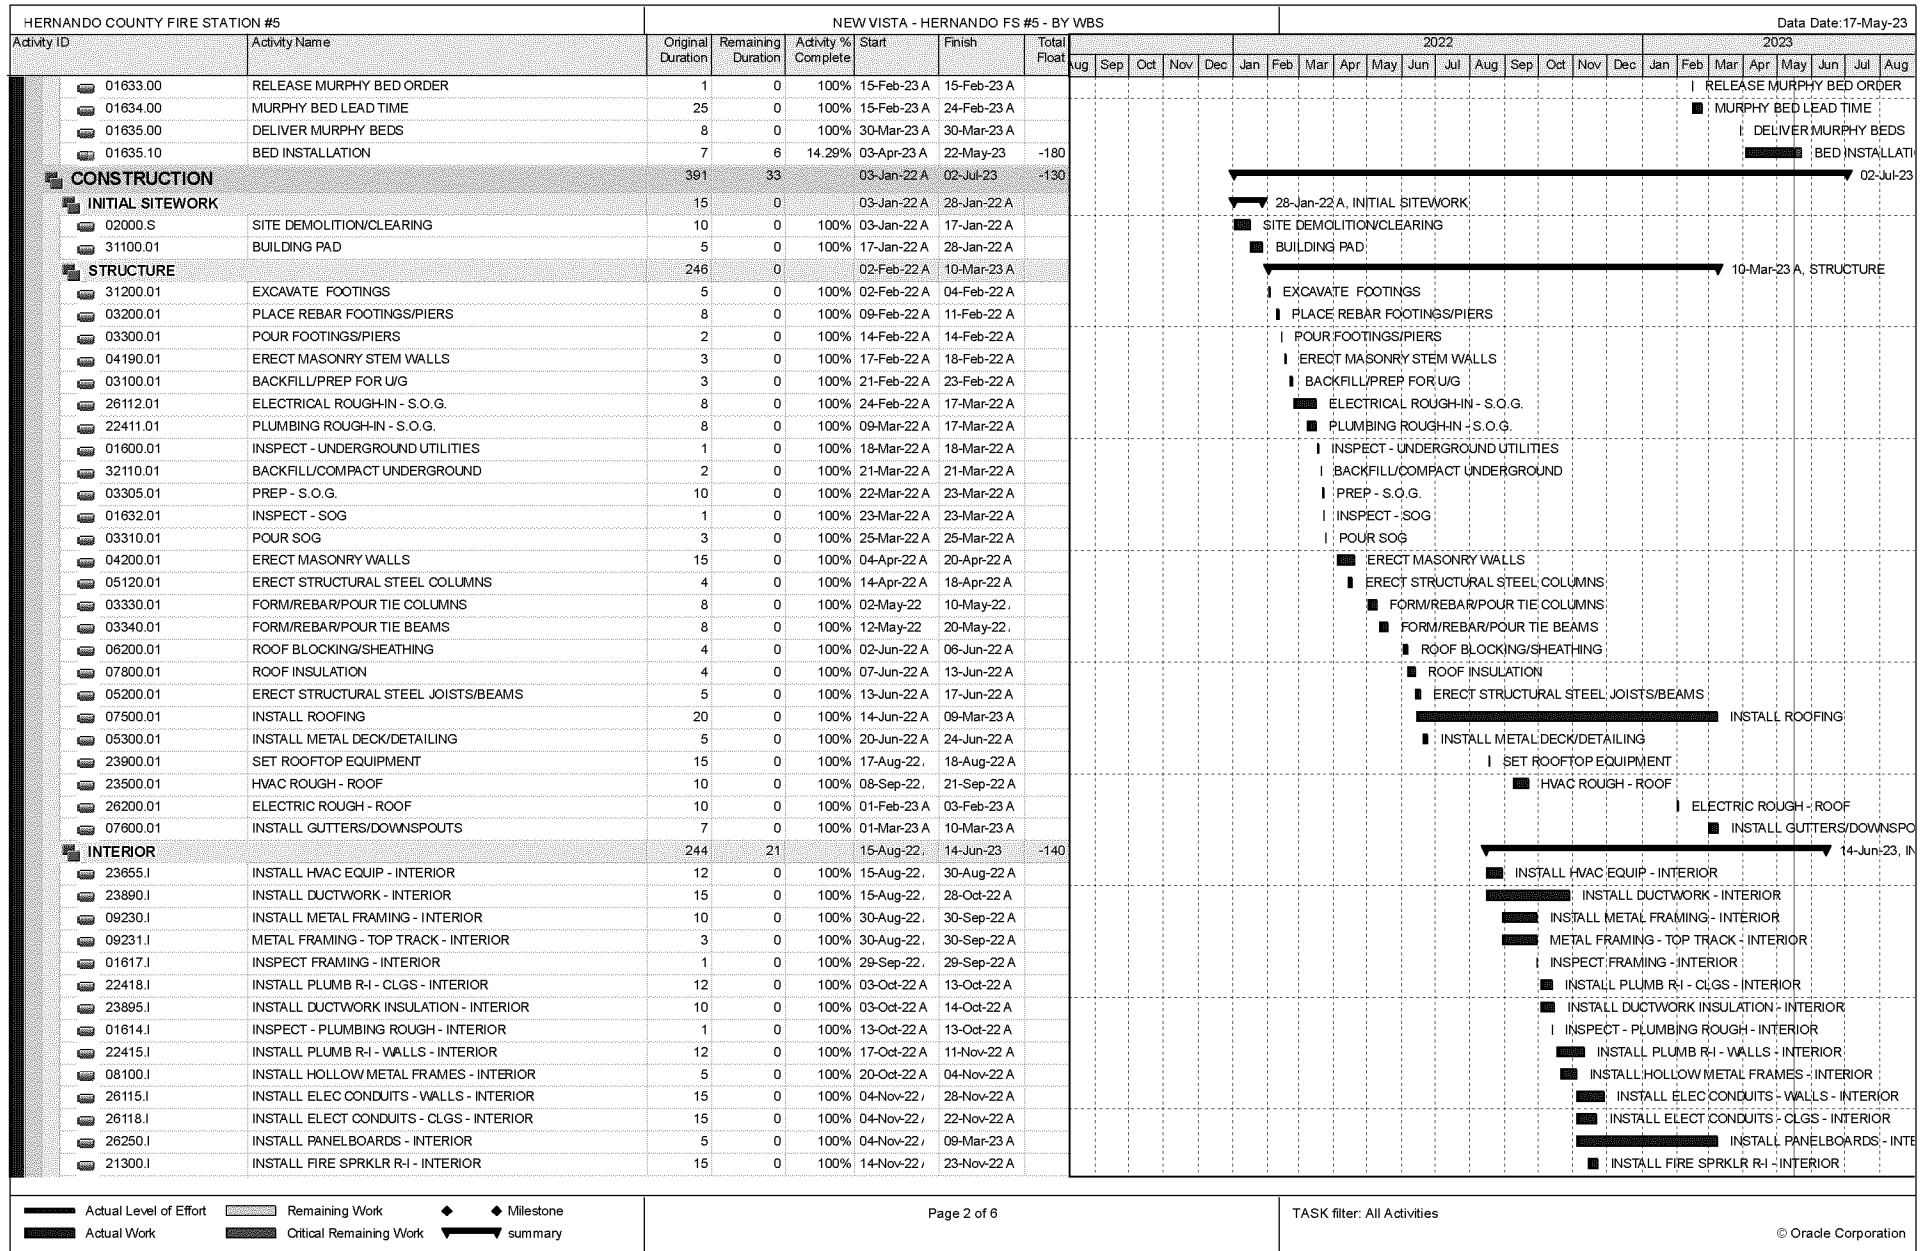


HERNANDO COUNTY FIRE STATION #5			NEW VISTA - HERNANDO FS #5 - BY WBS										Data Date: 17-May-23																											
Activity ID	Activity Name	Original Duration	Remaining Duration	Activity % Complete	Start	Finish	Total Float	2022														2023																		
								Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug								
26125.I	INSTALL ELECT WIRING - WALLS - INTERIOR	15	0	100%	14-Nov-22	30-Nov-22 A																														■	INSTALL ELECT WIRING - WALLS - INTERIOR			
26128.I	INSTALL ELECT WIRING- CLGS - INTERIOR	15	0	100%	14-Nov-22	30-Nov-22 A																														■	INSTALL ELECT WIRING- CLGS - INTERIOR			
27100.I	INSTALL COMMUNICATION SYSTEM R-I - INTERIOR	10	0	100%	14-Nov-22	24-Nov-22 A																														■	INSTALL COMMUNICATION SYSTEM R-I - INTERIOR			
23656.I	HVAC DUCT CONNECT/HOOK-UP - INTERIOR	5	0	100%	18-Nov-22	23-Nov-22 A																														■	HVAC DUCT CONNECT/HOOK-UP - INTERIOR			
23530.I	INSTALL HVAC PIPING - INTERIOR	10	0	100%	19-Nov-22	20-Nov-22 A																														■	INSTALL HVAC PIPING - INTERIOR			
10510.I	INSTALL LOCKERS - INTERIOR	5	0	100%	25-Nov-22	02-Dec-22 A																														■	INSTALL LOCKERS - INTERIOR			
01616.I	INSPECT - ELECTRIC ROUGH - INTERIOR	1	0	100%	30-Nov-22	30-Nov-22 A																														■	INSPECT - ELECTRIC ROUGH - INTERIOR			
23650.I	INSTALL KITCHEN EXHAUST - INTERIOR	4	0	100%	01-Dec-22	28-Feb-23 A																														■	INSTALL KITCHEN EXHAUST - INTERIOR			
23657.I	HVAC PIPING CONNECT/HOOK-UP - INTERIOR	5	0	100%	01-Dec-22	31-Jan-23 A																														■	HVAC PIPING CONNECT/HOOK-UP - INTERIOR			
09250.I	HANG/FINISH DRYWALL - INTERIOR	15	0	100%	05-Dec-22	31-Jan-23 A																														■	HANG/FINISH DRYWALL - INTERIOR			
07211.I	BUILDING INSULATION - INTERIOR	3	0	100%	14-Dec-22	06-Jan-23 A																														■	BUILDING INSULATION - INTERIOR			
08800.I	INSTALL INTERIOR GLAZING - INTERIOR	4	0	100%	03-Jan-23 A	13-Jan-23 A																														■	INSTALL INTERIOR GLAZING - INTERIOR			
21310.I	INSTALL FIRE SPRKLR HEADS/TRIM - INTERIOR	6	0	100%	03-Jan-23 A	17-Feb-23 A																														■	INSTALL FIRE SPRKLR HEADS/TRIM - INTERIOR			
09900.I	PAINT INTERIOR PRIME COAT - INTERIOR	7	0	100%	06-Jan-23 A	18-Jan-23 A																														■	PAINT INTERIOR PRIME COAT - INTERIOR			
28710.I	INSTALL FIRE ALARM TRIM/DEVICES - INTERIOR	6	0	100%	17-Jan-23 A	04-Feb-23 A																														■	INSTALL FIRE ALARM TRIM/DEVICES - INTERIOR			
09310.I	INSTALL CERAMIC TILE - INTERIOR	8	0	100%	13-Feb-23 A	08-Mar-23 A																														■	INSTALL CERAMIC TILE - INTERIOR			
26500.I	INSTALL ELEC FIXTURES - INTERIOR	12	0	100%	13-Feb-23 A	08-Mar-23 A																														■	INSTALL ELEC FIXTURES - INTERIOR			
26505.I	INSTALL ELEC TRIM - INTERIOR	7	0	100%	13-Feb-23 A	08-Mar-23 A																														■	INSTALL ELEC TRIM - INTERIOR			
09515.I	INSTALL ACOUSTICAL CLG TILE - INTERIOR	6	0	100%	20-Feb-23 A	03-Mar-23 A																														■	INSTALL ACOUSTICAL CLG TILE - INTERIOR			
01615.I	INSPECT - MEP - OVERHEAD - INTERIOR	1	0	100%	01-Mar-23 A	09-Mar-23 A																														■	INSPECT - MEP - OVERHEAD - INTERIOR			
09510.I	INSTALL ACOUSTICAL CLG GRID - INTERIOR	8	0	100%	01-Mar-23 A	07-Mar-23 A																														■	INSTALL ACOUSTICAL CLG GRID - INTERIOR			
23940.I	INSTALL HVAC GRILLS/TRIM - INTERIOR	8	0	100%	01-Mar-23 A	07-Mar-23 A																														■	INSTALL HVAC GRILLS/TRIM - INTERIOR			
09901.I	PAINT INTERIOR FINISH COAT - INTERIOR	10	0	100%	09-Mar-23 A	10-Mar-23 A																														■	PAINT INTERIOR FINISH COAT - INTERIOR			
10400.I	INSTALL SIGNAGE - INTERIOR	10	0	100%	10-Apr-23 A	21-Apr-23 A																														■	INSTALL SIGNAGE - INTERIOR			
09680.I	INSTALL FLOORING - INTERIOR	7	0	100%	02-May-23	04-May-23																														■	INSTALL FLOORING - INTERIOR			
10024.I	INSTALL FIRE EXTINGUISHERS - INTERIOR	10	5	50%	10-May-23	23-May-23	-125																													■	INSTALL FIRE EXTINGUISHERS - INTERIOR			
11310.I	INSTALL APPLIANCES - INTERIOR	10	4	60%	10-May-23	22-May-23	-139																													■	INSTALL APPLIANCES - INTERIOR			
22440.I	INSTALL PLUMB FIXTURES - INTERIOR	10	5	50%	10-May-23	23-May-23	-126																													■	INSTALL PLUMB FIXTURES - INTERIOR			
23980.I	START-UP HVAC SYSTEM - INTERIOR	10	5	50%	10-May-23	21-May-23	-199																													■	START-UP HVAC SYSTEM - INTERIOR			
06410.I	INSTALL CABINETS - INTERIOR	10	4	60%	12-May-23	22-May-23	-137																													■	INSTALL CABINETS - INTERIOR			
12200.I	INSTALL WINDOW SHADES - INTERIOR	11	11	0%	17-May-23	27-May-23	-199																													■	INSTALL WINDOW SHADES - INTERIOR			
12360.I	INSTALL COUNTERTOPS - INTERIOR	8	8	0%	17-May-23	26-May-23	-137																													■	INSTALL COUNTERTOPS - INTERIOR			
08810.I	INSTALL POLISHED GYM MIRRORS - INTERIOR	3	3	0%	22-May-23	24-May-23	-136																													■	INSTALL POLISHED GYM MIRRORS - INTERIOR			
10520.I	INSTALL SHELVING - INTERIOR	13	13	0%	22-May-23	07-Jun-23	-138																													■	INSTALL SHELVING - INTERIOR			
12230.I	INSTALL TV BRACKETS - INTERIOR	8	8	0%	22-May-23	31-May-23	-138																													■	INSTALL TV BRACKETS - INTERIOR			
23990.I	PERFORM TEST & BALANCE - INTERIOR	2	2	0%	22-May-23	23-May-23	-138																													■	PERFORM TEST & BALANCE - INTERIOR			
08200.I	HANG DOORS - INTERIOR (DELAY)	9	9	0%	25-May-23	06-Jun-23	-138																													■	HANG DOORS - INTERIOR (DELAY)			
10260.I	INSTALL WALL & DOOR PROTECTION - INTERIOR	13	13	0%	25-May-23	12-Jun-23	-136																													■	INSTALL WALL & DOOR PROTECTION - INTERIOR			
10800.I	INSTALL BATH ACCESSORIES - INTERIOR	9	9	0%	25-May-23	06-Jun-23	-132																													■	INSTALL BATH ACCESSORIES - INTERIOR			
08710.I	INSTALL FINISH HARDWARE - INTERIOR	2	2	0%	30-May-23	31-May-23	-138																													■	INSTALL FINISH HARDWARE - INTERIOR			
12500.I	INSTALL FURNITURE - INTERIOR	8	8	0%	05-Jun-23	14-Jun-23	-138																													■	INSTALL FURNITURE - INTERIOR			
■ APPARATUS BAY		226	3		04-Apr-22 A	19-May-23	-118																													■	APPARATUS BAY			
09231.AB	METAL FRAMING - TOP TRACK - APPARATUS BAY	2	0	100%	04-Apr-22 A	20-Apr-22 A																														■	METAL FRAMING - TOP TRACK - APPARATUS BAY			
22415.AB	INSTALL PLUMB R-I - WALLS - APPARATUS BAY	6	0	100%	10-Apr-22 A	05-May-22																														■	INSTALL PLUMB R-I - WALLS - APPARATUS BAY			
26115.AB	INSTALL ELEC CONDUITS - WALLS - APPARATUS BAY	8	0	100%	10-Apr-22 A	18-May-22																														■	INSTALL ELEC CONDUITS - WALLS - APPARATUS BAY			
08100.AB	INSTALL HOLLOW METAL FRAMES - APPARATUS BAY	4	0	100%	22-Apr-22 A	25-Apr-22 A																														■	INSTALL HOLLOW METAL FRAMES - APPARATUS BAY			
23655.AB	INSTALL HVAC EQUIP - APPARATUS BAY	7	0	100%	08-Aug-22	12-Aug-22 A																														■	INSTALL HVAC EQUIP - APPARATUS BAY			
09230.AB	INSTALL METAL FRAMING - APPARATUS BAY	5	0	100%	11-Aug-22	12-Aug-22 A																														■	INSTALL METAL FRAMING - APPARATUS BAY			
23890.AB	INSTALL DUCTWORK - APPARATUS BAY	8	0	100%	17-Aug-22	17-Sep-22 A												</																						

Actual Level of Effort
 Remaining Work
 Milestone
 Actual Work
 Critical Remaining Work
 summary

[illegible]

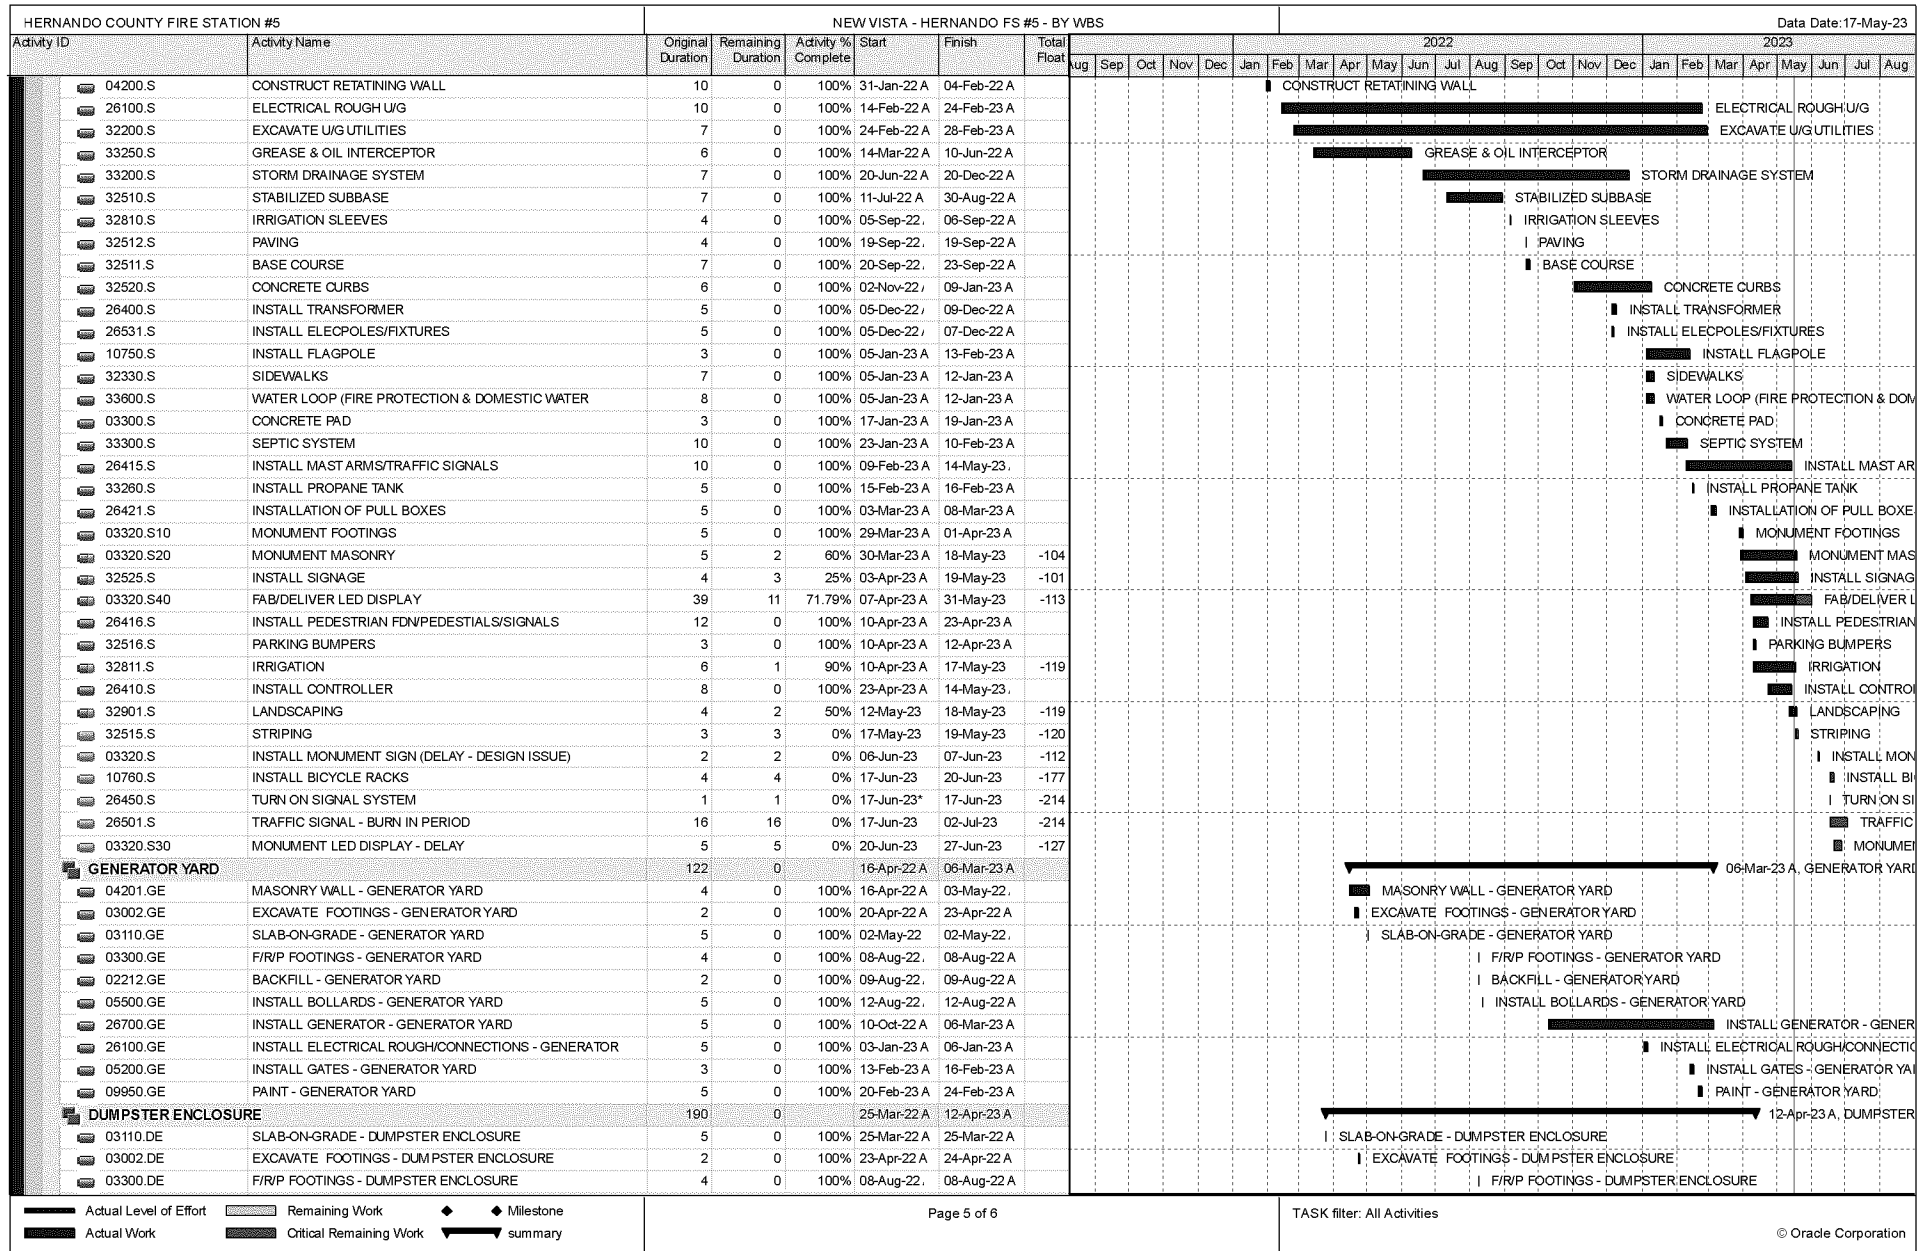

HERNANDO COUNTY FIRE STATION #5			NEW VISTA - HERNANDO FS #5 - BY WBS										Data Date: 17-May-23																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
Activity ID	Activity Name	Original Duration	Remaining Duration	Activity % Complete	Start	Finish	Total Float	2022												2023																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
								Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
	02212.DE BACKFILL - DUMPSTER ENCLOSURE	2	0	100%	09-Sep-22	10-Sep-22 A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Page 6 of 6

TASK filter: All Activities

© Oracle Corporation
